BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Project Division
Project Name	:	Improvements to Roads and Drains in Ward No.07 Byatarayanapura
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	9-Dec-20
Project End Date	:	5-Sep-21
Project Length in Months	:	9 Months

Sl. No	Assignment	Unit	Modified Schedule B Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Dismantling of existing structures like culverts,bridges, retaining walls and other structure comprising of masonry, cementconcrete, wood work, steel work, including T&P and scaffolding wherevernecessary,	Cum	2.64	2.64	100	10-12-20	12-12-20	2
2	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material,	Cum	1.44	1.44	100	10-12-20	12-12-20	2
3	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods	Cum	1115.80	1115.80	100	12-12-20	11-01-21	30
4	Providing and laying Plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted	Cum	922.53	922.53	100	16-12-20	14-05-21	149
5	Providing laying plain/ reinforced cement concrete for side Drains Using M20 nominal mix Concrete with OPC at 300kgs.With 20mm and Down size granite metal coarse aggregate at 0.69cum and fine aggregate at 0.43cum Machne mixed,	Cum	390.50	390.50	100	24-12-20	15-02-21	53
6	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire	Tonne	24.09	24.09	100	21-12-20	09-02-21	50
7	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,	Sqm	751.26	751.26	100	13-01-21	17-02-21	35
8	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc ,	Sqm	16.56	16.56	100	18-01-21	07-02-21	20
9	Dismantling of cement concrete pavement by mechanical means using pneumatic tools, breaking to pieces not exceeding 0.02 cum in volume and stock piling at designated locations and disposal of dismantled materials stacking serviceable and unserviceable materials seperately	Cum	1101.35	1101.35	100	09-02-21	06-03-21	25
10	Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and ,	Cum	191.48	191.48	100	14-02-21	16-03-21	30

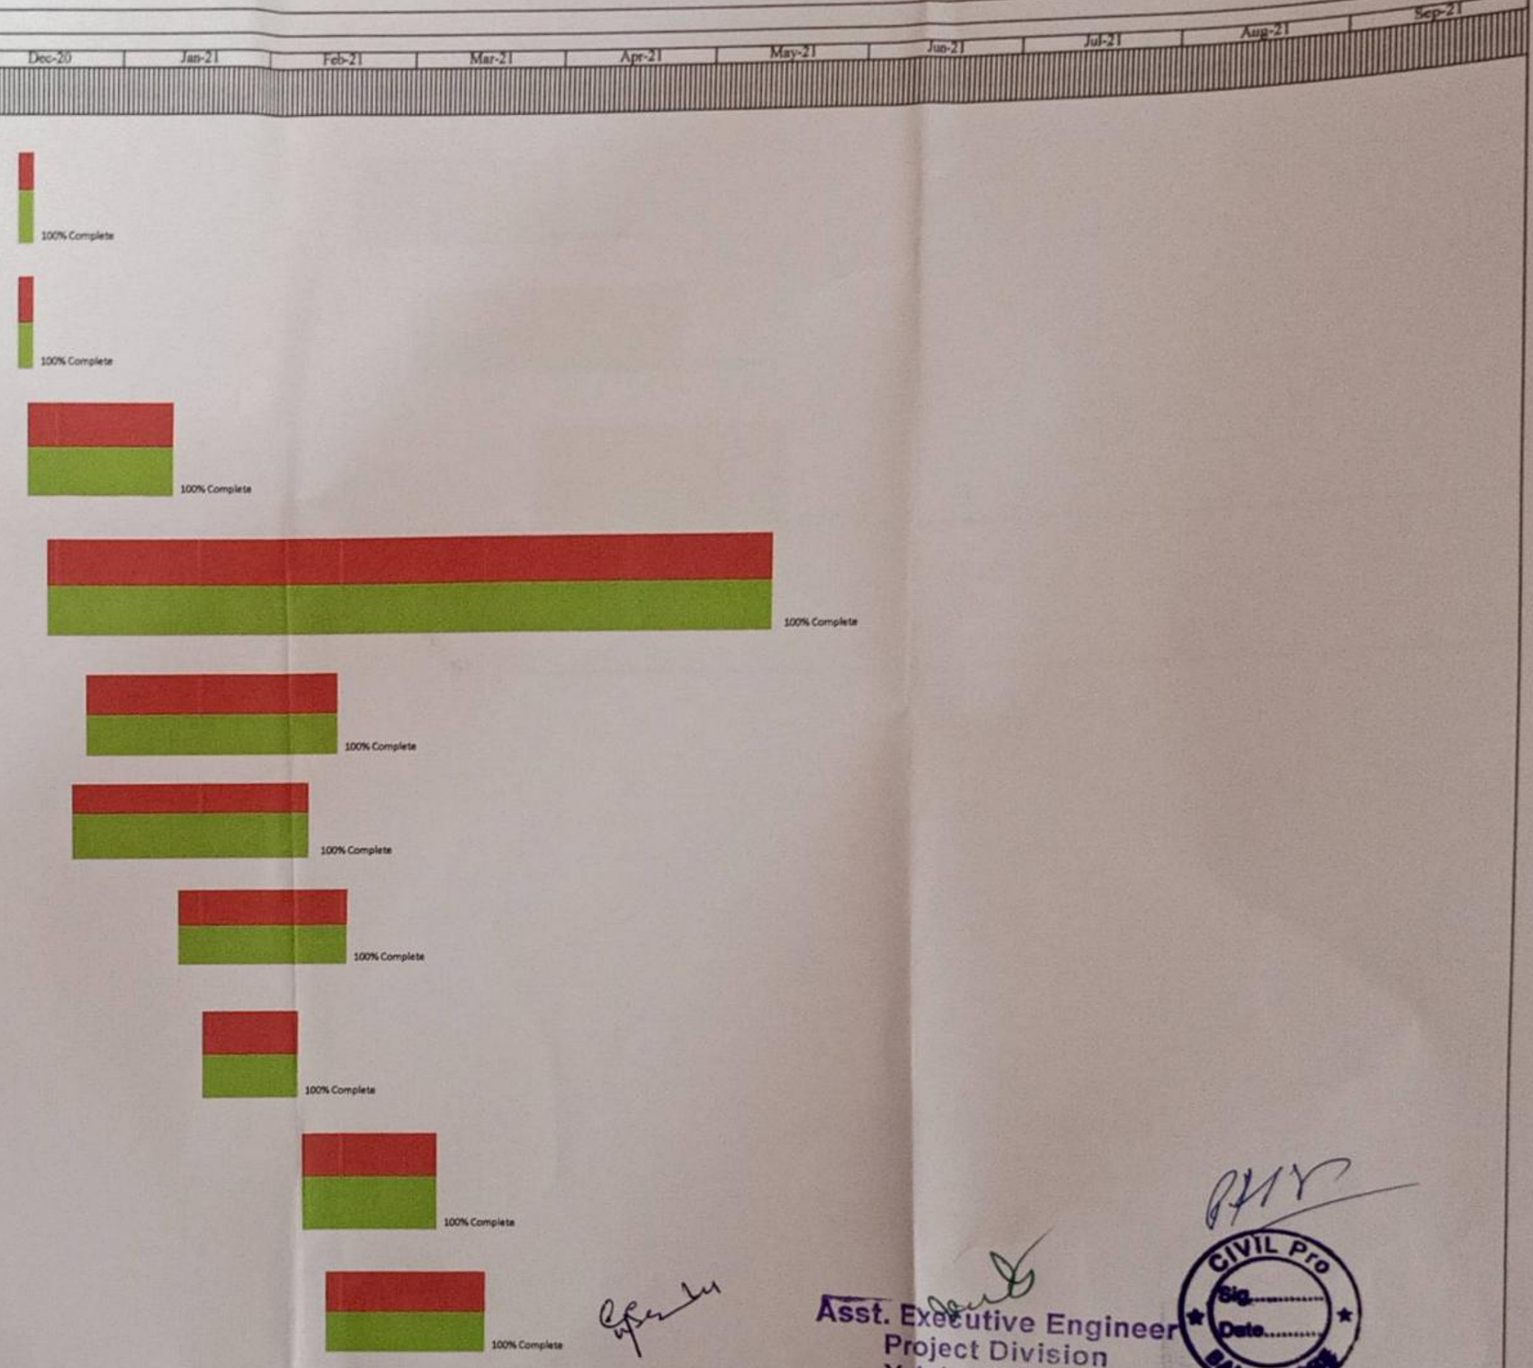

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

CIVIL Pro Sig. Date. BANGALORE

Scanned by TapScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Project Division
Project Name	:	Improvements to Roads and Drains in Ward No.07 Byatarayanapura
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	9-Dec-20
Project End Date	:	5-Sep-21
Project Length in Months	:	9 Months

Sl No	Assignment	Unit	Modified Schedule B Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
11	Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM	Sqm	4063.63	4063.63	100	19-02-21	31-03-21	40
12	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site,	Cum	191.65	191.65	100	01-03-21	25-04-21	55
13	Cement concrete pavement.Construction of un-reinforced plain cement concrete for pavement, using a grade concrete M30 over a prepared base with OPC course aggregate @ 0.69cum fine aggregate @ 0.46cum,course and fine aggregate confirming to IS:383-2016,	Cum	742.78	742.78	100	27-03-21	16-05-21	50

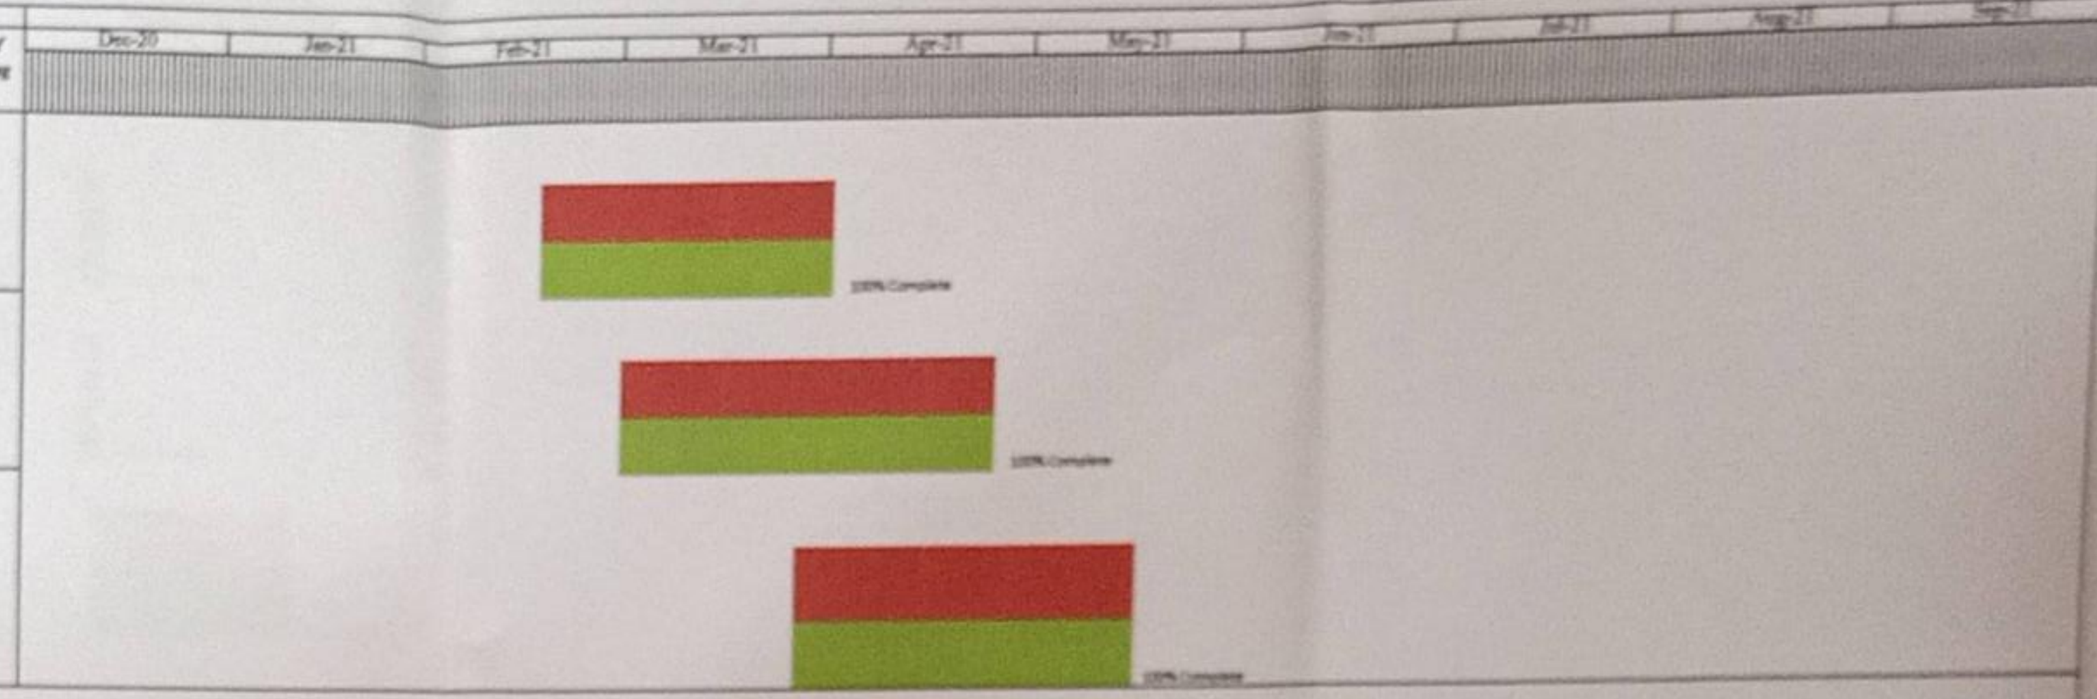

LEGEND

- Planned %
- Executed %

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

CIVIL Pro
Sig.
Date
BANGALORE

Scanned by TapScanner
